

**ASIKO TV**

THE SOUL OF AFRICA

— POC → MVP

From the 22-channel POC to a real MVP

The POC proves the idea in a browser. The MVP is the smallest version that is *real* — real channels, real ads, real reporting, that a sales house can plug into and a partner can go live on.

1 • What actually changes

LAYER	POC TODAY	MVP
Channels	HLS URLs played in the browser; "linear" faked by seeking a loop to the wall clock	Real 24/7 linear origin — Channel Engine (VOD2) 5–10 channels, from real content
Ads	Simulated break every 150s; the revenue panel is a model	Server-side ad insertion (Eyevinn SGAI) firing on SCTE-35, calling an ad decision server — first a tag, then a real SSP
EPG	Computed from a flat program list	Generated from a real dated schedule, delivered as an app
Analytics	Sample data in the Analytics preview	Real player beacons + ad-server + CDN logs → a monthly statement per channel
State	All in the browser's <code>localStorage</code>	A small backend for schedules, config, vote counts, analytics ingest
Front end	Desktop-first single page	Hardened: real mobile layout, error handling, correct banner, Terms/Privacy links, no simulated panels, public build
Domain	<code>github.io</code>	<code>asiko.africa</code> with HTTPS, plus one CTV surface (web-based Roku or a PWA)

LAYER	POC TODAY	MVP
Ops	None	Monitoring + alerting, as-run logging, a defined answer


What carries over unchanged: the player, the Browse view, the brand, the `channels.json` shape, the whole design. The MVP swaps the fake layers for real ones behind the same interface.

2 • The workstreams

#	WORKSTREAM	WHAT IT INVOLVES	OWNER
W1	Payout	Stand up Channel Engine (OSaaS or self-hosted on the KVM8). Provision 1 channel end to end, then clone to 5–10. Add a fallback slate and a backup source per channel.	ME
W2	Content	First real content: partner feeds + a starter licensed / public-domain library. Transcode to one consistent profile. Put it on Bunny behind a pull zone.	YOU + ME
W3	Ad insertion	Eyevinn SGAI in front of the channels. SCTE-35 driven from the schedule. Wire a test VAST tag, prove a break renders, then connect a real SSP / ad server.	ME
W4	Schedule & EPG	Replace the looped-list fake with a real dated schedule per channel. Generate an EPG feed; render it in the app.	ME + YOU (PROGRAMMIN
W5	Front-end hardening	Real mobile-portrait layout; move state to the backend; strip or gate the simulated revenue panel in the public build; consent banner; Terms / Privacy links; error & reconnect handling.	ME
W6	Measurement	A beacon endpoint + ingest + storage. First per-channel monthly statement. The partner portal is later (pilot phase).	ME
W7	Distribution	<code>asiko.africa</code> live (DNS), HTTPS, plus one CTV surface — a web-based Roku channel or a PWA.	YOU (DNS) +
W8	Light CMS	A way for non-engineers to edit schedules and channel config without touching code — a simple admin form over the backend, or a structured editor. Full CMS is Phase 2 / Enveu.	ME

#	WORKSTREAM	WHAT IT INVOLVES	OWNER
W9	Legal & consent	Cookie-consent banner (required before real programmatic ads), Privacy Policy + Terms drafted and linked.	YOU + LAWYER WIRES IT IN
W10	Ops	Uptime monitoring + alerting on the channels and the app, as-run logging, an on-call plan (you, a contractor, or Enveu managed ops).	YOU DECIDE; SETS UP MON

3 • Sequence & dependencies

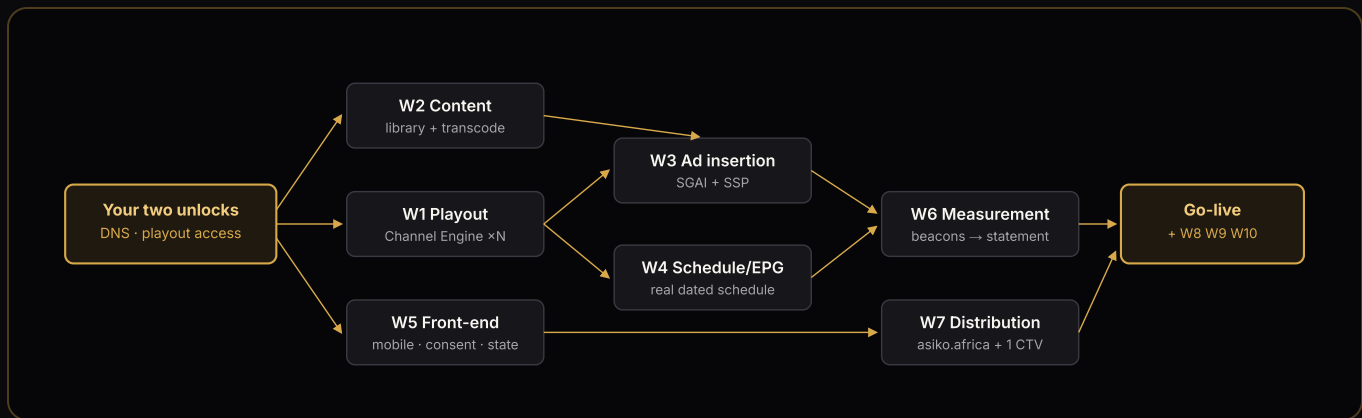

Nothing real starts until your two unlocks land — **DNS for asiko.africa** and **playlist access** (Eyevinn billing cleared or KVM8 SSH). After that, content and payout run in parallel; ad insertion and EPG follow payout; front-end, measurement, CMS, legal and ops run alongside and gate go-live.

4 • Timeline & effort

Roughly **6–8 weeks** from the two unlocks landing, most of it my build time, with your input on content, programming and the legal pack.

- ◆ **Weeks 1–2:** W1 one real channel end to end · W7 asiko.africa live · W5 mobile layout + consent
- ◆ **Weeks 3–4:** W1 clone to 5–10 channels · W2 real content in · W4 real schedules/EPG · W3 test ad tag proving a break
- ◆ **Weeks 5–6:** W3 real SSP wired · W6 beacons + first statement · W8 light CMS · one CTV surface
- ◆ **Weeks 7–8:** W9 legal linked · W10 monitoring · hardening · a partner goes live on a real channel

Cost stays modest — hundreds of dollars a month (playout, CDN, storage), plus one-off content/transcode and any legal fees. The big cheques (Enveu build, CTV apps, real content spend) are the *pilot* phase, committed against MVP numbers.

5 • In and out of MVP

In

- ◆ 5–10 real linear channels, 24/7, from real content, on `asiko.africa`
- ◆ Real SSAI with real demand; SCTE-35 from real schedules
- ◆ Real EPG; hardened web app with a proper mobile layout; consent + legal links
- ◆ Real measurement → a monthly per-channel statement
- ◆ One CTV surface; a light CMS; monitoring
- ◆ First invoice out; at least one partner channel genuinely live

Explicitly out — these are pilot / full-launch

- ◆ Native CTV apps across Roku / Fire TV / Samsung / LG
- ◆ A full multi-user CMS (Enveu scope)
- ◆ Live DVR / catch-up / start-over
- ◆ A real voting backend (the competition rows stay a mock)
- ◆ The partner self-service portal (statements are PDF in MVP)
- ◆ VOD / TVOD / SVOD
- ◆ Scaling past ~10 channels

6 • Exit criteria — when MVP is done

- ◆ 5–10 channels running 24/7 without manual intervention, with slate failover proven
- ◆ An ad break rendered from a real SSP on a real channel, measured
- ◆ A monthly statement a sales house looked at and trusted
- ◆ The demo on `asiko.africa`, working on a phone
- ◆ One external channel partner live end to end via their own feed

- ♦ A first invoice issued — however small

Hit those and the pilot phase — CTV apps, real ad-sales pipeline, the Enveu build — is fundable against evidence instead of a forecast.

Asiko TV — POC to MVP transition

Media Icons Africa · 7 September 2026 · companion to the Trail to Launch and Week 1 Plan
